BUILD WITH AGENTS

Project Proposal for *Get Path*

Get Path partners with WithAgents to design and build their product, delivered with agents — a working product shipped fast on transparent, pay-as-you-go weekly terms.

PREPARED BY **WithAgents** FOR **Get Path** WA-GETPATH-20260617 ISSUED JUNE 17, 2026 VALID JULY 17, 2026

FULL BUILD

$15,000

20 hrs/week @ $100/hr over 8 weeks. AI/agent costs included.

RECOMMENDED INITIAL BUILD · RECOMMENDED

$10,000

Lean 5-week core (100 hrs), flexible across a 5–10 weeks range as scope evolves.

OVERVIEW

Goals

Get Path is an AI-powered career and learning-pathway web app that turns a person's current skills and target role into a personalized, step-by-step skill roadmap. It serves early-career professionals and career-changers who know where they want to go but not how to get there.

G1 · Personalized roadmaps

Let any user go from a target role to a concrete, ordered skill roadmap in under five minutes.

G2 · Trustworthy AI recommendations

Generate roadmap steps grounded in a curated skills graph so suggestions feel credible rather than generic.

G3 · Visible progress

Give users a clear way to track which roadmap milestones they have completed and what comes next.

G4 · Validated v1 launch

Ship a lean, production-deployed MVP that real users can sign up for and complete an end-to-end roadmap flow.

SCOPE

Deliverables & tasks

D1 · Foundation & Project Setup — 13h

Stand up the application skeleton, repository, environments, and CI so all later work lands on a stable, deployable base.

Scaffold Next.js app, repo, linting, and folder conventions	Foundation	5h
Provision Postgres + hosting and wire staging/production environments	Foundation	4h
Set up CI pipeline, env-var management, and preview deploys	Foundation	4h

D2 · Authentication & User Profiles — 17h

Email-based account creation and a profile that captures the user's current skills and target role, which feed the recommendation engine.

Implement email/password auth with sessions and password reset	Foundation	6h
Build profile data model (current skills, target role, experience level)	Core Features	5h
Create profile onboarding UI and skill/role input flow	Core Features	6h

D3 · Skills Graph & Roadmap Data Model — 18h

The curated skills/role knowledge graph and roadmap schema that the AI grounds its recommendations against, plus seed content for launch.

Design skills/roles graph schema and roadmap/milestone tables	Core Features	6h
Seed curated skills graph for 3 launch career tracks	Core Features	7h
Build roadmap CRUD + persistence and milestone status tracking	Polish & UX	5h

D4 · AI Roadmap Recommendation Engine — 23h

The core differentiator: an LLM/agent integration that reads the user's profile and the skills graph to assemble a personalized, ordered roadmap.

Define prompt + retrieval flow that grounds the LLM in the skills graph	AI Integration	7h
Implement agent orchestration to assemble and order roadmap steps	AI Integration	8h
Add output validation, guardrails, and graceful fallbacks	AI Integration	5h
Tune ranking and add caching to control latency and token cost	AI Integration	3h

D5 · Roadmap UI & Progress Experience — 15h

The interactive roadmap view where users explore their generated path, mark milestones complete, and regenerate or refine their roadmap.

Build interactive roadmap visualization with milestone detail panels	Polish & UX	7h
Implement progress tracking, completion state, and dashboard	Polish & UX	5h
Add roadmap regeneration/refine flow and responsive polish	Polish & UX	3h

D6 · Testing, Launch & Handoff — 14h

End-to-end validation of the core flow, production deployment, and a clean handoff so the client can operate and extend Get Path.

End-to-end validation of signup-to-roadmap flow on staging	Launch & Handoff	5h
Production deploy, monitoring, and analytics instrumentation	Launch & Handoff	5h
Handoff: docs, runbook, and walkthrough session	Launch & Handoff	4h

ASSUMPTIONS

- Client provides brand assets (logo, colors, fonts) and approved copy for the three launch career tracks.
- Scope is a single responsive web platform; no native mobile app.
- Client supplies or approves an LLM provider API key and accepts usage-based AI costs.
- A single English-language locale is sufficient for v1.
- Subject-matter input for the curated skills graph is available from the client or a designated expert.
- One staging and one production environment are sufficient for launch.

CONSTRAINTS


- v1 is web-only and English-only.
- Recommendations are limited to the three seeded career tracks at launch.
- Email/password authentication only; no third-party SSO in this build.
- AI roadmap generation is grounded in the curated skills graph rather than open-ended web browsing.
- Fixed five-week timeline aligned to the five delivery phases.

OUT OF SCOPE

- Native iOS and Android applications.
- Single sign-on (Google/GitHub/SAML) and enterprise identity integration.
- Payments, subscriptions, or billing.
- Integrations with external course catalogs or job boards.
- Multi-language / localization support.
- Admin CMS for non-technical editing of the skills graph.

ESTIMATIONS

Effort by phase

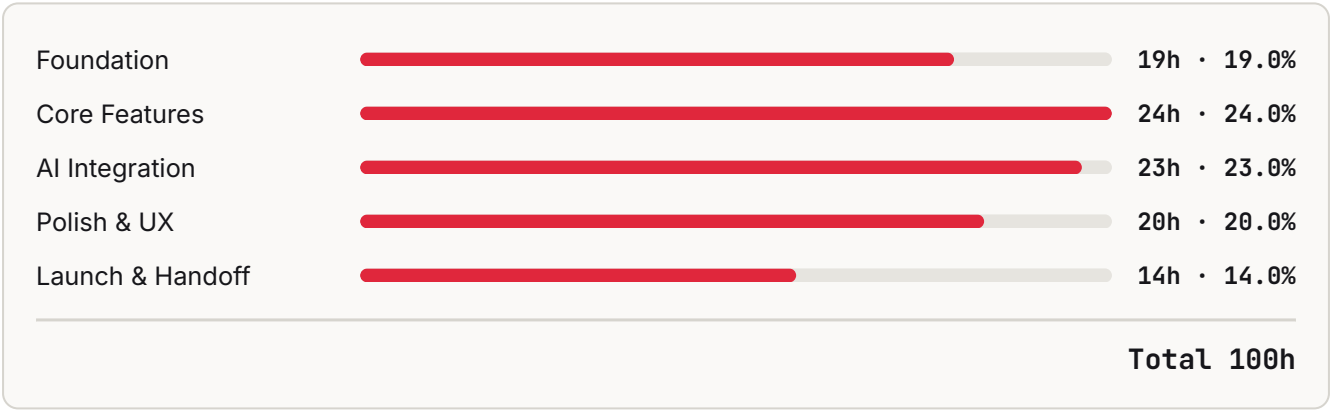

TIMELINE

5-week core · starts Monday, June 22, 2026

Flexible across a 5–10 weeks range.

WEEK	FOCUS	DATES	DELIVERABLES	HOURS
Week 1	**Foundation**	Jun 22 – Jun 26	D1, D2	**19h**
Week 2	**Core Features**	Jun 29 – Jul 3	D2, D3	**24h**
Week 3	**AI Integration**	Jul 6 – Jul 10	D4	**23h**
Week 4	**Polish & UX**	Jul 13 – Jul 17	D3, D5	**20h**
Week 5	**Launch & Handoff**	Jul 20 – Jul 24	D6	**14h**

COSTS

Investment & payment plan

BUILD LINE ITEM	AMOUNT
Foundation & Project Setup 13 hrs @ $100/hr	**$1,300**
Authentication & User Profiles 17 hrs @ $100/hr	**$1,700**
Skills Graph & Roadmap Data Model 18 hrs @ $100/hr	**$1,800**
AI Roadmap Recommendation Engine 23 hrs @ $100/hr	**$2,300**
Roadmap UI & Progress Experience 15 hrs @ $100/hr	**$1,500**
Testing, Launch & Handoff 14 hrs @ $100/hr	**$1,400**
AI / agent runtime + tooling Model usage, agent orchestration, and dev tooling	**included**
Recommended initial build	**$10,000**

WEEKLY PAYMENT SCHEDULE · PAY-AS-YOU-GO

WHEN	MILESTONE	INVOICE	CUMULATIVE
Wk 1–2	Kickoff · Foundation + Core Features	$4,000	$4,000
Wk 3	AI Integration	$2,000	$6,000
Wk 4	Polish & UX	$2,000	$8,000
Wk 5	Launch & Handoff	$2,000	$10,000

DOWN PAYMENT

$4,000

First 2 weeks of work.

REMEDIATION

$100/hr

Post-build changes and fixes billed hourly, only as used.

CHANGE BUDGET

$5,000

Reserve for product evolution after the initial build ships.

TERMS

How we work together

Down payment

A $4,000 down payment kicks off the engagement and covers the first 2 weeks of work.

Weekly billing

After the down payment, work is billed at $2,000/week (20 hrs @ $100/hr) as it progresses — pay-as-you-go, pause or adjust between weeks.

Remediation

Post-build changes and fixes are billed at $100/hour, only as used — no retainer.

Change budget

A $5,000 reserve is set aside for product evolution after the initial build ships, drawn down only against agreed work.

build with agents — Timely delivery, pay-as-you-go weekly rates.
